0LAUK0: Robots Everywhere

Group 05

Project Start: Mon, 19/4/2021
Today: Fri, 18/6/2021
Display Week: 2
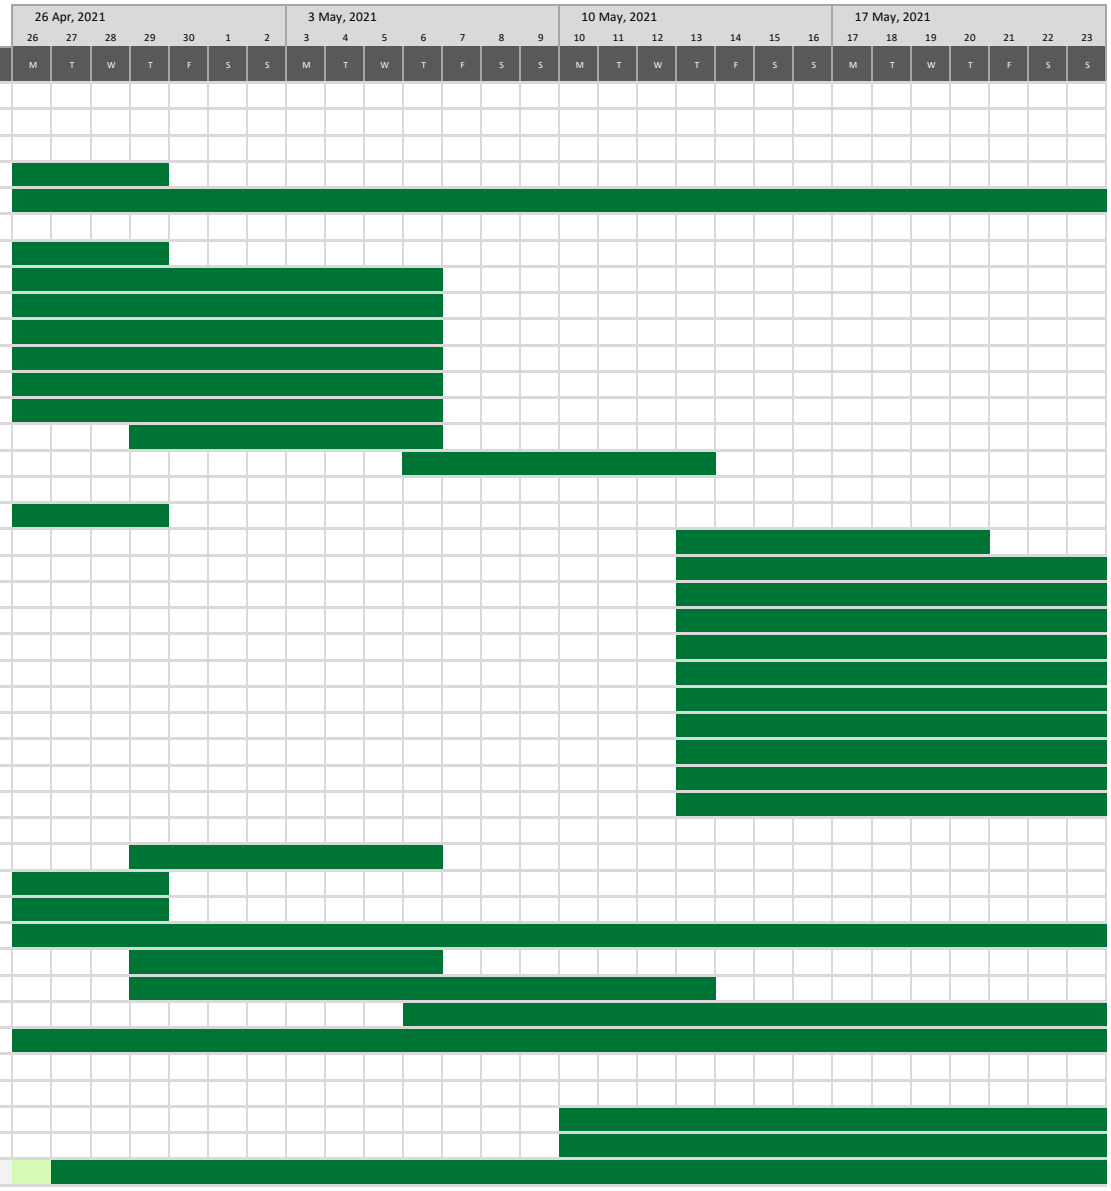
TASK	ASSIGNED TO	PROGRESS	START	END
Planning				
Planning: Develop Milestones	All	100%	19/4/21	22/4/21
Planning: Project Plan	Quentin	95%	22/2/21	29/4/21
Planning: Fix and addapt plan	Quentin	10%	4/2/21	18/6/21
Research				
Research: State of the art (papers as project referal)	All		19/4/21	29/4/21
Research: Space and Orbital knowledge	Tim		19/4/21	6/5/21
Research: Previously planned missions to Titan	Ive		22/4/21	6/5/21
Research: Conditions for 'life'	Peter		22/4/21	6/5/21
Research: Scanner types and how they can be used	Quentin		22/4/21	6/5/21
Research: Potential Software/material needed to realise deliverable	Johan		22/4/21	6/5/21
Research: How can data samples be collected	Peter		22/4/21	6/5/21
Research: Programming method for deliverable	Quentin		29/4/21	6/5/21
Research: Communication methods (for technical deliverable)	Ive		6/5/21	13/5/21
Deliverables:				
Deliverables: Type of deliverable (T = Technical ; (P) = Program)	All		22/4/21	29/4/21
Deliverables: Datasets	Tim		13/5/21	20/5/21
Deliverables: Communication system	Ive		13/5/21	27/5/21
Deliverables (T): Working camera mount	Peter		13/5/21	27/5/21
Deliverables (T): Potential virtual testing environment	Peter		13/5/21	27/5/21
Deliverables (T): Multi-varied terrain mobility	Johan		13/5/21	27/5/21
Deliverables (T): Potential testing methods	Tim		13/5/21	27/5/21
Deliverables (P): Software decision (what will be used to create program)	All		13/5/21	27/5/21
Deliverables (P): Mapping system	Quentin		13/5/21	27/5/21
Deliverables (P): create a suitible 'memory'	Johan		13/5/21	27/5/21
Deliverables (P): Development in goal based decision making	Ive		13/5/21	27/5/21
Deliverables (P): Development in self learning system	Quentin		13/5/21	27/5/21
Wiki Page:				
WIki Page: Topics to be covered in wiki	All		29/4/21	6/5/21
Wiki Page: Project description	Tim		22/4/21	29/4/21
WIki Page: Project Plan	Quentin		22/4/21	29/4/21
Wiki Page: Logbook	All		19/4/21	18/6/21
Wiki Page: Project Method	Peter		29/4/21	6/5/21
WIki Page: Research	All		29/4/21	13/5/21
WIki Page: Deliverable development	Johan		6/5/21	18/6/21
WIki Page: Literature ans Sources	All		22/4/21	18/6/21
Final Deadlines:				
Final Deadlines: Presentation	All	0%	10/6/21	18/6/21
Final Deadlines: Completed Deliverable	All	0%	10/5/21	18/6/21
Final Deadlines: Demonstration of functioning deliverable	All	0%	10/5/21	18/6/21
Final Deadlines: Completed Gantt Diagram	All	10%	22/4/21	18/6/21
